# GROUP ASSESSMENT ITEM COVER SHEET

| Student Numbers: | Emails: | FIRST NAMES | FAMILY / LAST NAMES |
|---|---|---|---|
| 3503338 | DhimanshiPiripun.Jayasena@uon.edu.au | Dhimanshi | Jayasena |
| 3511138 | HariKrishna.Jadda@uon.edu.au | Hari Krishna | Jadda |
| 3528532 | MadhaviLatha.Tripuram@uon.edu.au | Madhavi Latha | Tripuram |
| 3504807 | Premshanker.Vanam@uon.edu.au | Prem | Vanam |
| 3508025 | sankeerth.sappa@uon.edu.au | Sankeerth | Sappa |

| Course Code | Course Title |
|---|---|
| INFT6304 | Project Planning and Management |
| *(Example)* ABCD1234 | *(Example)* Intro to University |

Campus of Study: Callaghan (eg Callaghan, Ourimbah, Port Macquarie)

Assessment Item Title: Assessment 3 - Project Planning and Implementation Due Date/Time: 03.08.2025

Tutorial Group (If applicable): Group 11 Word Count (If applicable):

Lecturer/Tutor Name: Professor Caroline Chan

Extension Granted: ☐ Yes ☐ No Granted Until:

Please attach a copy of your extension approval

**NB: STUDENTS MAY EXPECT THAT THIS ASSIGNMENT WILL BE RETURNED WITHIN 3 WEEKS OF THE DUE DATE OF SUBMISSION**

**Please tick box if applicable**

☐ *Students within the Faculty of Business and Law, Faculty of Science, Faculty of Engineering and Built Environment and the School of Nursing and Midwifery:* We verify that we have completed the online Academic Integrity Module and adhered to its principles.

☐ *Students within the School of Education:* We understand that a minimum standard of correct referencing and academic literacy is required to pass all written assignments in the School of Education; and we have read and understood the School of Education *Course Outline Policy Supplement,* which includes important information related to assessment policies and procedures.

We declare that this assessment item is our own work unless otherwise acknowledged and is in accordance with the University's Student Academic Integrity Policy

We certify that this assessment item has not been submitted previously for academic credit in this or any other course. We certify that we have not given a copy or have shown a copy of this assessment item to another student enrolled in the course, other than members of this group.

We acknowledge that the assessor of this assignment may, for the purpose of assessing this assignment:

- Reproduce this assessment item and provide a copy to another member of the Faculty; and/or
- Communicate a copy of this assessment item to a plagiarism checking service (which may then retain a copy of the item on its database for the purpose of future plagiarism checking).
- Submit the assessment item to other forms of plagiarism checking.

We certify that any electronic version of this assessment item that we have submitted or will submit is identical to this paper version.

Turnitin ID: (if applicable)

**DATE STAMP HERE**

Insert this way

| Signature: | Date: |
|---|---|
| Dhimanshi | 03.08.2025 |
| Hari Krishna | 03.08.2025 |
| Madhavi Latha | 03.08.2025 |
| Prem | 03.08.2025 |
| Sankeerth | 03.08.2025 |

# Assignment 3

# Project Planning and Implementation

# DXP-SmartGovNSW

## Table of Contents:

1. Introduction and Recap of Assessment 2

2. Work Breakdown Structure (WBS)

3. Project Schedule

4. Resource Plan and Budget Overview

5. Risk Management Plan

6. Stakeholder Engagement and Communication Plan

7. Project Monitoring and Change Control Strategy

8. Team and Individual Reflection

9. References

## 1. Introduction and Recap of Assessment 2:

This document presents the comprehensive Project Planning and Execution Strategy for the Digital Experience Platform (DXP) for SmartGovNSW, building upon the foundational work established in Assessment 2. The initial assessment focused on justifying the strategic imperative of this initiative, outlining the critical need for a unified and enhanced digital customer experience for NSW citizens. This report now translates that justification into a detailed and practical project management plan, demonstrating how the proposed solution will be effectively implemented.

The DXP project is a pivotal digital transformation effort aimed at significantly improving how NSW citizens interact with government services. The core client needs, as articulated in the Request for Proposal (RFP), revolved around enhancing customer satisfaction and engagement, reducing operational costs, and accelerating the delivery of digital services. Assessment 2 established the project's strong strategic alignment with the NSW Government's broader digital transformation agenda, particularly the Digital Transformation Strategy 2025 and the Cloud-First Policy, by fostering a "digital by default" approach to public service delivery.

As articulated above, the key objectives of the DXP included implementing one DXP for more than 500,000 users, increasing customer satisfaction by 25%, reducing operational costs by 20%, and reducing the time to implement new digital services by 40%. Initially, the project was scoped out in three phases: Discovery, Design and Implementation, and Ongoing Support and Maintenance. A hybrid project management approach was recommended to combine traditional governance, which provides stability and compliance, and an Agile method of iterative development and adaptive planning. This strategic planning document now elaborates those initial ideas into a detailed road map for implementation.


## 2. Work Breakdown Structure (WBS):

A Work Breakdown Structure is a hierarchical decomposition of the total project scope which the project team will undertake to achieve the project objectives and create the required deliverables. It is a hierarchical structure which is deliverable-oriented to define all of the work necessary to complete the project and is a basis for planning, scheduling, allocating resources, and estimating project costs. In the case of the DXP-SmartGovNSW project, the WBS has been laid out to show a hybrid approach that concurrently combined the traditional phases Discovery, Design & Implementation, Support with iterative development cycles within the implementation phase.

### *2.1.WBS Structure:*

The DXP-SmartGovNSW project WBS is organized into three main levels, with the project as the highest level, followed by major phases, and then key deliverables and work packages. This structure ensures that all necessary work is captured and assigned, providing a clear roadmap for execution. The WBS is presented below in a hierarchical text format, with explanations for each major element.

***Work Break down Structure diagram:***

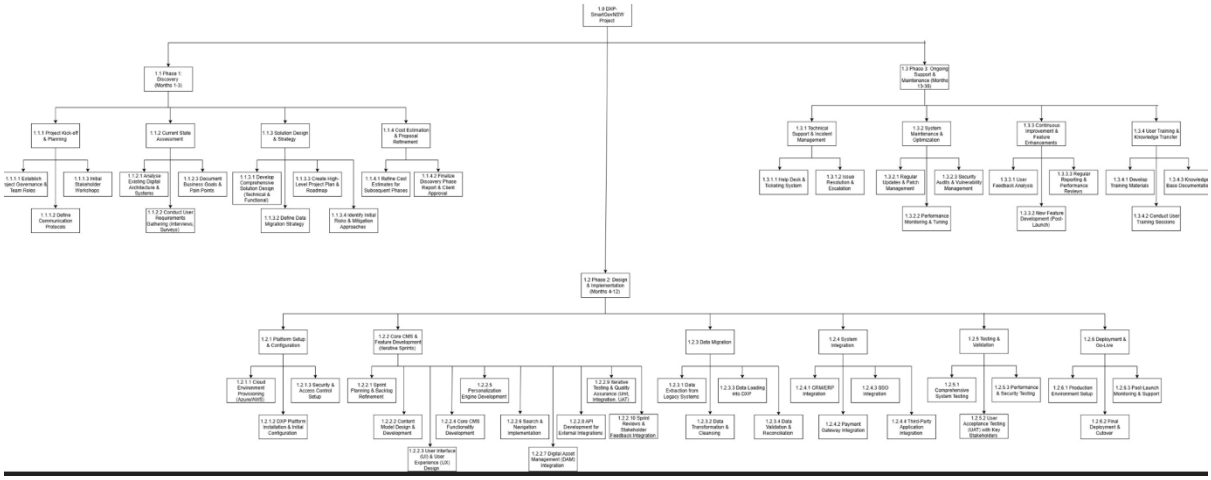

**1.0 DXP-SmartGovNSW Project**

**1.1 Phase 1: Discovery (Months 1-3)**

1.1.1 Project Kick-off & Planning

1.1.1.1 Establish Project Governance & Team Roles

1.1.1.2 Define Communication Protocols

1.1.1.3 Initial Stakeholder Workshops

1.1.2 Current State Assessment

1.1.2.1 Analyse Existing Digital Architecture & Systems

1.1.2.2 Conduct User Requirements Gathering (Interviews, Surveys)

1.1.2.3 Document Business Goals & Pain Points

1.1.3 Solution Design & Strategy

1.1.3.1 Develop Comprehensive Solution Design (Technical & Functional)

1.1.3.2 Define Data Migration Strategy

1.1.3.3 Create High-Level Project Plan & Roadmap

1.1.3.4 Identify Initial Risks & Mitigation Approaches

1.1.4 Cost Estimation & Proposal Refinement

1.1.4.1 Refine Cost Estimates for Subsequent Phases

1.1.4.2 Finalize Discovery Phase Report & Client Approval

**1.2 Phase 2: Design & Implementation (Months 4-12)**

1.2.1 Platform Setup & Configuration

1.2.1.1 Cloud Environment Provisioning (Azure/AWS)

1.2.1.2 DXP Platform Installation & Initial Configuration

1.2.1.3 Security & Access Control Setup

1.2.2 Core CMS & Feature Development (Iterative Sprints)

1.2.2.1 Sprint Planning & Backlog Refinement

1.2.2.2 Content Model Design & Development

1.2.2.3 User Interface (UI) & User Experience (UX) Design

1.2.2.4 Core CMS Functionality Development

1.2.2.5 Personalization Engine Development

1.2.2.6 Search & Navigation Implementation

1.2.2.7 Digital Asset Management (DAM) Integration

1.2.2.8 API Development for External Integrations

1.2.2.9 Iterative Testing & Quality Assurance (Unit, Integration, UAT)
1.2.2.10 Sprint Reviews & Stakeholder Feedback Integration

1.2.3 Data Migration

1.2.3.1 Data Extraction from Legacy Systems

1.2.3.2 Data Transformation & Cleansing

1.2.3.3 Data Loading into DXP

1.2.3.4 Data Validation & Reconciliation

1.2.4 System Integration

1.2.4.1 CRM/ERP Integration

1.2.4.2 Payment Gateway Integration

1.2.4.3 SSO Integration

1.2.4.4 Third-Party Application Integration

1.2.5 Testing & Validation

1.2.5.1 Comprehensive System Testing

1.2.5.2 User Acceptance Testing (UAT) with Key Stakeholders
1.2.5.3 Performance & Security Testing

1.2.6 Deployment & Go-Live

1.2.6.1 Production Environment Setup

1.2.6.2 Final Deployment & Cutover

1.2.6.3 Post-Launch Monitoring & Support

**1.3 Phase 3: Ongoing Support & Maintenance (Months 13-36)**

1.3.1 Technical Support & Incident Management

1.3.1.1 Help Desk & Ticketing System

1.3.1.2 Issue Resolution & Escalation

1.3.2 System Maintenance & Optimization

1.3.2.1 Regular Updates & Patch Management

1.3.2.2 Performance Monitoring & Tuning

1.3.2.3 Security Audits & Vulnerability Management

1.3.3 Continuous Improvement & Feature Enhancements

1.3.3.1 User Feedback Analysis

1.3.3.2 New Feature Development (Post-Launch)

1.3.3.3 Regular Reporting & Performance Reviews

1.3.4 User Training & Knowledge Transfer

1.3.4.1 Develop Training Materials

1.3.4.2 Conduct User Training Sessions

1.3.4.3 Knowledge Base Documentation

## *2.2. Explanation of Major WBS Elements:*

### *1.1 Phase 1: Discovery:*

This initial phase is crucial for laying a solid foundation for the entire project. It involves understanding the client's existing infrastructure, gathering detailed user requirements, and formulating a comprehensive solution design. The output of this phase is a refined project plan and detailed cost estimates for subsequent phases, culminating in client approval to proceed.

### *1.2 Phase 2: Design & Implementation:*


This is the core development phase, where the DXP platform is set up, configured, and populated with content and integrations. This phase will largely follow an Agile methodology, with iterative sprints for feature development, continuous testing, and regular stakeholder feedback. This iterative approach allows for flexibility and adaptation to evolving requirements, ensuring that the delivered solution remains aligned with user needs. Key activities include platform setup, core CMS and feature development, data migration, system integration, and comprehensive testing before deployment.


### *1.3 Phase 3: Ongoing Support & Maintenance:*

This long-term phase ensures the sustained performance, security, and relevance of the DXP. It encompasses technical support, regular system maintenance, continuous performance optimization, and the development of new features based on user feedback and evolving government needs. User training and knowledge transfer are also critical components to ensure internal teams can effectively manage and utilize the platform.

# 3. Project Schedule:

The project schedule for the DXP-SmartGovNSW project is designed to ensure timely delivery while accommodating the iterative nature of the Agile development within the hybrid framework. The overall project duration is estimated to be 36 months, aligning with the initial contract term, with the core implementation phase targeted for completion within 12 months. The schedule below outlines key activities, their estimated durations, and critical milestones.

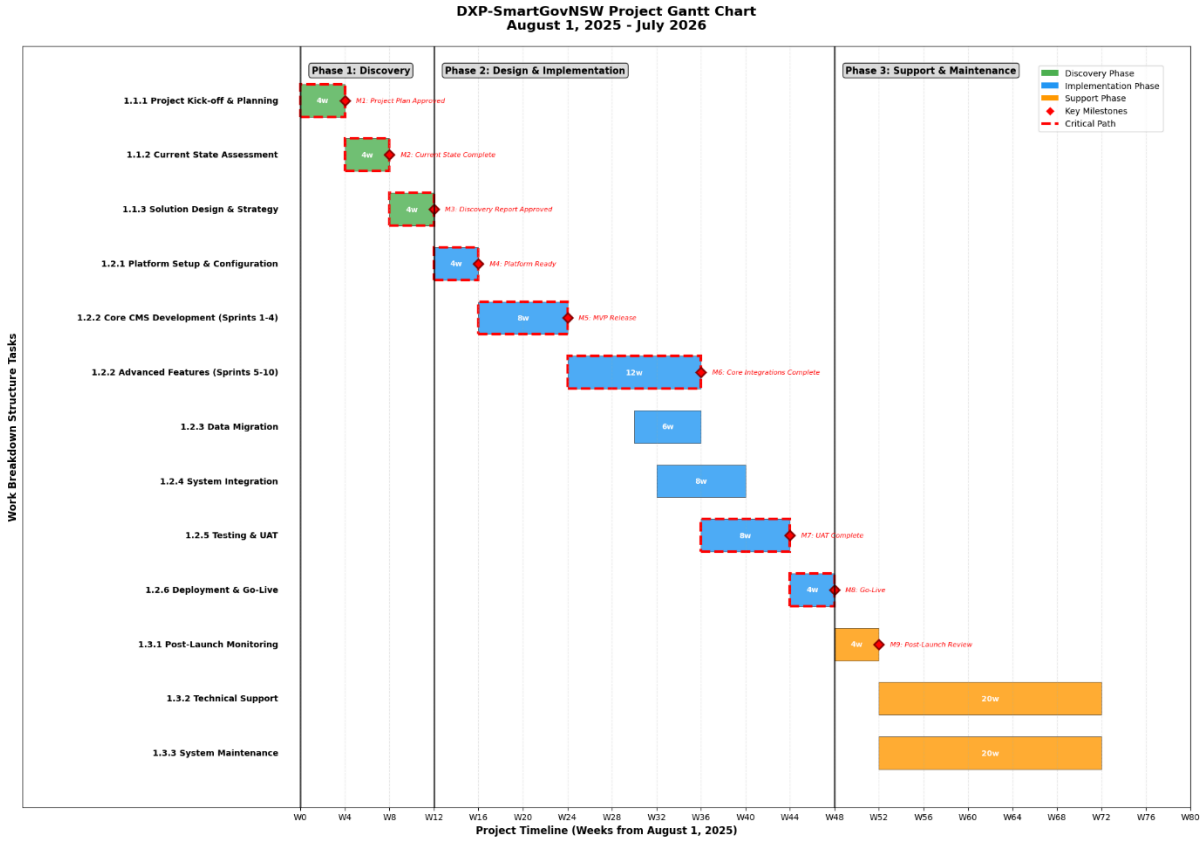
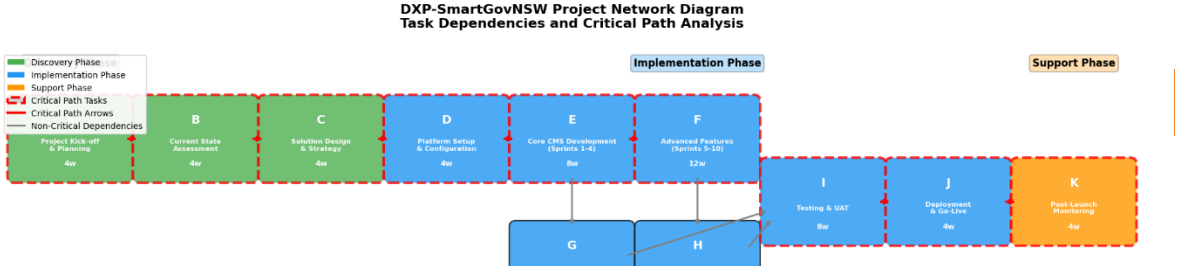
### Critical Path Analysis:

A → B → C → D → E → F → I → J → K

**Duration:** 52 weeks (1 year for core implementation)

**Float:** 0 weeks (any delay impacts project completion)

### Milestones:

Month 1: Project Plan Approved (Week 4)

Month 2: Current State Complete (Week 8)

Month 3: Discovery Report Approved (Week 12)

Month 4: Platform Ready (Week 16)

Month 5: MVP Release (Week 24)

Month 6: Core Integrations Complete (Week 36)

Month 7: UAT Complete (Week 44)

Month 8: Go-Live (Week 48)

Month 9: Post-Launch Review (Week 52)

### Project Timeline:

**Start Date:** August 1, 2025

**Implementation End:** July 31, 2026 (48 weeks)

**Support Phase:** August 2026 - July 2028

**Total Duration:** 156+ weeks (3 years)

## *3.1 Project Timeline Overview:*

| Phase | Duration | Key Activities | Milestones | Dependencies |
|---|---|---|---|---|
| 1. Discovery | Months 1-3 | Project Kick-off, Current State Assessment, Solution Design, Cost Estimation | M1: Project Plan Approved (End Month 1), M2: Solution Design Approved (End Month 2), M3: Discovery Report & Phase 2 Approval (End Month 3) | No dependency |
| 2. Design & Implementation | Months 4-12 | Platform Setup, Core CMS & Feature Development (Sprints), Data Migration, System Integration, Testing, Deployment | M4: MVP Release (End Month 6), M5: Core Integrations Complete (End Month 9), M6: UAT Complete (End Month 11), M7: Go-Live (End Month 12) | Month 3 |
| 3. Ongoing Support & Maintenance | Months 13-36 | Technical Support, System Maintenance, Continuous Improvement, User Training | M8: Post Launch Review (End Month 13), M9: Annual Performance Review (End Month 24 & 36) | Month 7 |

## *3.2. Detailed Schedule Breakdown (Weekly/Monthly Focus)*

### Phase 1: Discovery (Weeks 1-12):

**Weeks 1-4:** Project Kick-off, Team Onboarding, Initial Stakeholder Workshops, Establish Governance.

Milestone: Project Plan Approved (End Week 4).

**Weeks 5-8:** Current State Analysis (Technical & Business), User Requirements Gathering, Data Analysis.

Milestone: Current State Assessment Complete (End Week 8).

**Weeks 9-12:** Solution Design & Architecture, Data Migration Strategy, High-Level Project Plan, Initial Risk Assessment, Refine Cost Estimates.

Milestone: Solution Design Approved & Discovery Report Submitted (End Week 12).

### Phase 2: Design & Implementation (Weeks 13-48):

**Weeks 13-16:** Platform Setup & Initial Configuration (Cloud Environment, DXP Installation, Security).

Milestone: Platform Ready for Development (End Week 16).

**Weeks 17-24 (Sprints 1-4):** Core CMS Development, Content Model Design, Initial UI/UX, First Integrations example SSO.

Milestone: MVP Release (End Week 24). This MVP will include core CMS functionality and 2 key integrations, allowing for early user feedback and validation.

**Weeks 25-36 (Sprints 5-10):** Advanced Feature Development (Personalization, Search, DAM), Remaining System Integrations CRM, ERP, Payment Gateway, Data Migration Planning & Execution.

Milestone: Core Integrations Complete (End Week 36).

**Weeks 37-44 (Sprints 11-14):** Comprehensive System Testing, User Acceptance Testing (UAT) with key stakeholders, Performance & Security Testing.

Milestone: UAT Complete (End Week 44).

**Weeks 45-48:** Production Environment Setup, Final Deployment, Go-Live Activities, Post-Launch Monitoring Setup.

Milestone: Go-Live (End Week 48).

### Phase 3: Ongoing Support & Maintenance (Weeks 49-156)

**Weeks 49-52:** Initial Post-Launch Monitoring, Hypercare Support, Post-Launch Review.
Milestone: Post-Launch Review (End Week 52).

**Ongoing (Monthly/Quarterly):** Technical Support, System Updates, Performance Tuning, Security Audits, Continuous Improvement Sprints for new features, User Training & Knowledge Transfer.

Milestone: Annual Performance Review (End Month 24 & 36).

### *3.3. Key Aspects of the Schedule:*

• ***Major Milestone Dates:*** The schedule is punctuated by critical milestones Month 1- Month 9 that represent significant project achievements and client approval points. These milestones serve as crucial checkpoints for progress assessment and decision-making.

• ***Client Approval Points:*** Client approval is explicitly required at the end of the Discovery Phase Month 3 and upon the successful completion of UAT Month 6. These points ensure continuous alignment with client expectations and provide formal gateways for progression.

• ***Critical Activities and Critical Path:*** The critical path, representing the longest sequence of activities that must be completed on time for the project to finish on schedule, will be dynamically managed throughout the project. In the initial phases, activities related to solution design, platform setup, and core CMS development are anticipated to be on the critical path. During the iterative development sprints, the critical path will shift based on dependencies and resource availability. Any delays in critical activities will directly impact the overall project timeline.

• ***Agile Milestones:*** The inclusion of an "MVP Release" Month 4 by Month 6 is a key Agile milestone. This early delivery of core functionality allows for immediate user feedback and validation, mitigating risks and ensuring that the project delivers value incrementally. The "Core Integrations Complete" Month 5 milestone signifies the successful connection of the DXP with essential government systems.

### *3.4. Assumptions Made in Scheduling:*

**Resource Availability:** It is assumed that all required project team members development, QA, project management, business analysis and client-side resources subject matter experts, UAT participants will be available as per the project plan and dedicated to their respective tasks.

**Client Responsiveness:** Timely feedback and approvals from SmartGovNSW stakeholders are assumed, particularly at key approval points Month 3 and Month 6. Delays in client responsiveness could impact the schedule.

**Third-Party Vendor Performance:** The timely delivery and quality of services or products from third-party vendors example DXP platform provider, integration partners are assumed to meet contractual obligations.

**Data Quality and Accessibility:** It is assumed that legacy data required for migration is accessible and of sufficient quality, minimizing the need for extensive data cleansing efforts beyond what is planned.

**Technical Environment Stability:** The stability of the development, testing, and production environments cloud infrastructure, network connectivity is assumed to be consistent and reliable.

**Scope Stability:** While the hybrid approach allows for flexibility, significant changes to the core project scope beyond planned iterative refinements are assumed to be managed through a formal change control process and may impact the schedule and budget.

# 4. Resource Plan and Budget Overview:

Effective resource allocation and accurate budget estimation are critical components of a successful project planning and execution strategy. This section outlines the human, technical, and financial resources required for the DXP-SmartGovNSW project, providing a high-level cost estimate and the underlying assumptions. The aim is to ensure that the project is adequately resourced to meet its objectives while maintaining fiscal responsibility and transparency.

## *4.1.Resource Plan:*

The DXP-SmartGovNSW project will require a diverse team with specialized skills across various domains, complemented by essential technical infrastructure and tools. The resource plan is designed to support the hybrid project management approach, ensuring both the structured governance and the agile delivery needs are met.

### *4.1.1. Personnel Resources:*

The project team will comprise a mix of internal SmartGovNSW personnel and external vendor specialists, leveraging existing expertise while bringing in specialized DXP implementation knowledge. The core team roles and their primary responsibilities are outlined below:

| Role | Key Responsibilities | Allocation (FTE) | Phase Involvement |
|---|---|---|---|
| Project Manager | Overall project planning, execution, monitoring, control, stakeholder communication, risk management, team leadership. | 1.0 | All Phases |
| Solution Architect | Design of DXP architecture, technical oversight, integration strategy, ensuring scalability and security. | 0.8 | Discovery, Design & Implementation |

| | | | |
|---|---|---|---|
| Business Analyst(s) | Requirements gathering, process mapping, user story creation, liaison between business and technical teams. | 1.5 | Discovery, Design & Implementation |
| DXP Developers (Backend) | API development, database integration, core platform customization, microservices development. | 3.0 | Design & Implementation |
| DXP Developers (Frontend) | UI/UX implementation, responsive design, content presentation, user journey optimization. | 2.0 | Design & Implementation |
| QA Engineer(s) | Test strategy, test case development, manual and automated testing, defect management, performance testing. | 1.5 | Design & Implementation, Support |
| Data Migration Specialist | Data extraction, transformation, loading (ETL), data quality assurance, reconciliation. | 1.0 | Design & Implementation |
| Integration Specialist | API integration with CRM, ERP, payment gateways, SSO, third-party applications. | 1.0 | Design & Implementation |
| Security Specialist | Security architecture review, vulnerability assessment, compliance, access control implementation. | 0.5 | All Phases |
| Training & Documentation Specialist | Development of training materials, user guides, knowledge base articles, conducting training sessions. | 0.5 | Design & Implementation, Support |
| Content Strategist | Content model design, content | 0.5 | Discovery, Design & Implementation |

| | | | |
|---|---|---|---|
| | migration planning, content governance. | | |

FTE (Full-Time Equivalent) represents the approximate dedication of a resource to the project. Some roles may be shared or scaled based on project phase and workload. The team composition reflects the need for diverse skill sets, as highlighted in the initial team formation, covering development, testing, project management, and technical analysis.

### *4.1.2 Technical Resources and Tools:*

Beyond human capital, the project requires a robust technical environment and a suite of tools to facilitate efficient development, collaboration, and deployment:

• ***DXP Platform License:*** Selection and licensing of a suitable DXP platform example Adobe Experience Platform, Sitecore, Optimizely, or an open-source alternative like Liferay DXP that meets the technical requirements outlined in the RFP.

• ***Cloud Infrastructure:*** Provisioning of cloud services Azure or AWS for hosting the DXP, including compute, storage, networking, and managed services for databases and analytics. This aligns with the NSW Government's cloud-first policy.

• ***Development Tools:*** Integrated Development Environments (IDEs), version control systems example Git, and continuous integration/continuous deployment (CI/CD) pipelines.

• ***Collaboration & Project Management Tools:*** Jira for agile project management, Confluence for documentation, and communication platforms example Microsoft Teams, Slack for real-time collaboration. These tools support the transparent communication practices emphasized in the stakeholder engagement strategy.

• ***Testing Tools:*** Automated testing frameworks example Selenium, Cypress, performance testing tools example JMeter, and security scanning tools.

• ***Analytics & Monitoring Tools:*** Built-in DXP analytics, cloud provider monitoring dashboards example Azure Monitor, AWS CloudWatch, and third-party APM (Application Performance Monitoring) tools.

## *4.2.High-Level Budget Estimates:*

The project budget is estimated based on a combination of personnel costs, software licenses, infrastructure, and other operational expenses. Given the high-level nature of this planning document, these are initial estimates and will be refined during the Discovery phase (Phase 1) and subsequent iterative planning cycles. The total estimated budget for the three-year contract term is approximately AUD 8-12 million, broken down as follows:

| Category | Estimated Cost Range (AUD) | Notes |
|---|---|---|
| Personnel (Internal & External) | 5,000,000 - 7,500,000 | Includes salaries for internal staff, and consulting fees for external DXP specialists, developers, and QA. This is the largest component. |
| DXP Platform Licensing | 1,500,000 - 2,500,000 | Annual licensing fees for the chosen DXP platform over the three-year contract. Varies significantly by vendor and features. |
| Cloud Infrastructure (Azure/AWS) | 800,000 - 1,200,000 | Costs for compute, storage, networking, managed services, and data transfer over three years. Optimized for scalability and cost efficiency. |
| Third-Party Integrations & APIs | 300,000 - 500,000 | Costs associated with integrating with existing CRM, ERP, payment gateways, and other third party systems. May include API usage fees. |
| Software & Tools (Non-DXP) | 100,000 - 200,000 | Licenses for project management software, testing tools, security tools, and other development utilities. |
| Training & Knowledge Transfer | 50,000 - 100,000 | Development of training materials, workshops, and ongoing support for SmartGovNSW staff. |
| Contingency Reserve | 500,000 - 1,000,000 | A reserve of 10-15% of the total estimated cost to cover unforeseen expenses, scope changes, or risks. This aligns with best practices in project management for managing uncertainty. |
| **Total Estimated Budget** | **8,250,000 - 13,000,000** | **This range provides flexibility and accounts for potential variations in vendor selection and specific implementation complexities.** |

### *4.3. Key Cost-Related Insights and Assumptions:*

• ***Hybrid Approach Cost-Efficiency:*** The hybrid project management approach is expected to optimize costs by leveraging Agile for rapid development and value delivery, reducing the risk of costly rework due to changing requirements. Traditional governance ensures controlled spending and adherence to budget limits for the overall project. The phased rollout strategy also allows for early realization of benefits and incremental investment decisions.

• ***Cloud Cost Optimization:*** The budget assumes a continuous focus on cloud cost optimization strategies, including right-sizing instances, utilizing reserved instances where appropriate, and leveraging serverless architectures for specific components to minimize operational expenses.

• ***Resource Utilization:*** The budget assumes optimal utilization of both internal and external resources. Any significant deviations in resource availability or productivity could impact the overall cost.

• ***Scope Stability:*** While the project embraces iterative development, the core scope defined in the RFP and refined in the Discovery phase is assumed to remain relatively stable. Major scope changes not covered by the contingency reserve would necessitate a formal change request and potential budget revision.

• ***Vendor Selection:*** The budget range accounts for variations in DXP vendor pricing. A detailed vendor selection process during the Discovery phase will aim to secure the most cost-effective solution that meets all technical and functional requirements.

• ***Inflation and Exchange Rates:*** The estimates are based on current market rates and do not explicitly account for significant inflation or adverse exchange rate fluctuations over the three-year period. These factors would be monitored and addressed as part of ongoing financial management.

## 5. Risk Management Plan:

Effective risk management is fundamental to navigating the inherent uncertainties of large scale digital transformation projects like the DXP-SmartGovNSW. This section outlines a proactive approach to identifying, assessing, and responding to potential risks. The hybrid project management approach, integrating Agile principles, plays a crucial role in mitigating delivery risks and fostering adaptability.

### *5.1. Identified Risks and Mitigation Strategies:*

Risk is defined as an uncertain event or condition that, if it occurs, has a positive or negative effect on a project's objectives. The DXP project will employ a continuous risk management process, encompassing identification, assessment, response development, and control. This iterative process ensures that risks are actively monitored and managed throughout the project lifecycle. Based on the project scope, technical complexity, and

stakeholder landscape, the following significant risks have been identified. For each, the likelihood probability of occurrence and impact consequence if it occurs are assessed, and practical mitigation or response strategies are proposed.

| Risk ID | Risk Description | Likelihood | Impact | Mitigation/Response Strategy |
|---|---|---|---|---|
| R1 | Scope Creep: Uncontrolled expansion of project requirements beyond the initial agreed upon scope, leading to budget overruns and schedule delays. | Medium | High | **Mitigation:** Implement a strict change control process detailed in Section 7.2. Utilize Agile sprints with fixed timeboxes and clearly defined deliverables. Prioritize features using MoSCoW method. Conduct regular stakeholder reviews to manage expectations and validate scope. Any new requirements beyond sprint scope will be added to the product backlog for future consideration and formal approval. |
| R2 | Integration Challenges: Difficulty integrating the DXP with existing legacy systems CRM, ERP, payment gateways due to technical complexities, outdated APIs, or data inconsistencies. | High | High | **Mitigation:** Conduct a thorough technical assessment of all legacy systems during the Discovery phase. Develop a detailed integration strategy with clear API specifications. Utilize an API-first DXP architecture. Conduct early and continuous integration testing. Allocate dedicated integration specialists to the project. Agile Mitigation: Incremental integration, where small parts of the system are integrated and tested in each sprint, allowing for early detection and resolution of integration issues. |
| R3 | Low User Adoption: Citizens or internal staff do not fully adopt the new DXP due to poor user experience, lack of training, or resistance to change. | Medium | High | **Mitigation:** Prioritize user centric design (UI/UX) based on extensive user research and co-design workshops. Provide comprehensive training programs and easily accessible support resources FAQs, chatbots. Develop a robust communication plan to highlight benefits and address concerns. Implement a phased rollout to allow users to adapt gradually. Agile Mitigation: Continuous user feedback loops through UAT and sprint reviews, allowing for rapid adjustments to improve usability and address user pain points. |

| | | | | |
|---|---|---|---|---|
| R4 | Data Migration Errors: Inaccurate, incomplete, or corrupted data during migration from legacy systems to the new DXP, leading to data integrity issues. | Medium | High | **Mitigation:** Develop a detailed data migration plan, including data cleansing, transformation, and validation procedures. Utilize automated migration tools where possible. Conduct multiple dry runs of data migration. Implement strict data quality checks and reconciliation processes post-migration. Engage data governance experts. |
| R5 | Resource Unavailability/Skill Gaps: Key project team members or required specialists are unavailable or lack the necessary skills, impacting project progress and quality. | Medium | Medium | **Mitigation:** Conduct thorough resource planning and secure commitments early. Implement cross-training and knowledge transfer within the team. Develop a contingency plan for critical roles, including identifying potential external contractors. Foster a culture of continuous learning and professional development. Agile Mitigation: Cross functional teams reduce reliance on single points of failure. Daily stand-ups and retrospectives help identify resource bottlenecks and skill gaps early, allowing for proactive adjustments. |
| R6 | Security Vulnerabilities: The DXP or its integrations are susceptible to cyber threats, leading to data breaches, system downtime, or reputational damage. | High | High | **Mitigation:** Implement security-by-design principles throughout the development lifecycle. Conduct regular security audits, penetration testing, and vulnerability assessments. Adhere to NSW Government data security frameworks and industry best practices. Implement robust access controls, encryption, and multi-factor authentication. |

## *5.2. Agile's Role in Mitigating Delivery Risks:*

As highlighted in the risk table, Agile methodologies inherently mitigate several delivery risks. The iterative and incremental nature of Agile development allows for:

• ***Early Detection of Issues:*** By delivering working software frequently example in bi-weekly sprints, technical and integration issues are identified and resolved much earlier in the project lifecycle, reducing the cost and effort of rework compared to traditional waterfall approaches.

• ***Adaptability to Change:*** Agile embraces change as an inevitable part of complex projects. Instead of resisting changes, the framework provides mechanisms example product backlog refinement, sprint planning to incorporate new requirements or adjust priorities efficiently, minimizing the impact of evolving needs on the project.

• ***Continuous Feedback:*** Regular sprint reviews and user acceptance testing (UAT) sessions provide continuous feedback from stakeholders and end-users. This ensures that the product being built truly meets their needs, reducing the risk of delivering a solution that does not align with expectations.

• ***Improved Collaboration and Communication:*** Daily stand-ups, co-location where possible, and transparent communication tools example Jira dashboards foster strong collaboration within the team and with stakeholders, reducing communication breakdowns and misunderstandings that can lead to project risks.

• ***Reduced Scope Creep:*** While Agile welcomes changing requirements, the fixed timebox of sprints and the focus on delivering a Minimum Viable Product (MVP) help manage scope creep by ensuring that only the highest priority features are developed within a given iteration. New features are added to the backlog and prioritized for future sprints, preventing uncontrolled expansion.

## 6. Stakeholder Engagement and Communication Plan:

Effective stakeholder management is paramount to the success of the DXP-SmartGovNSW project. A comprehensive understanding of stakeholder roles, interests, and influence is essential for navigating the complex landscape of government digital transformation. This section outlines a detailed strategy for engaging with key stakeholders, ensuring enhanced communication and collaboration. The strategy emphasizes proactive engagement, transparent communication, and the integration of Agile principles to foster a collaborative environment where all stakeholders feel heard and valued.

### *6.1. Stakeholder Identification and Analysis:*

A thorough stakeholder analysis has been conducted to identify all individuals and groups who have an interest in or will be affected by the DXP project. The stakeholders have been categorized based on their level of power influence and interest in the project, which informs the tailored engagement strategies outlined below. The following table provides a summary of key stakeholders, their roles, and their respective levels of power and interest:

| Stakeholder Group | Role/Interest | Power | Interest | Engagement Strategy |
|---|---|---|---|---|

| | | | | |
|---|---|---|---|---|
| Project Sponsor<br><br>Example: Head of Digital Transformation | Provides funding, strategic direction, and ultimate approval | High | High | Manage Closely:<br>Regular one-on one meetings, detailed progress reports, and direct involvement in key decisions. |
| NSW Government Agencies Example: Service NSW, Transport for NSW | Key users of the DXP, providing services to citizens | High | High | Keep Satisfied: Regular workshops, dedicated communication channels, and representation in project governance bodies. |
| Project Team | Responsible for the design, development, and implementation of the DXP | High | High | Keep Informed & Engaged: Daily stand-ups, sprint planning and reviews, and collaborative tools example Jira, Confluence. |
| IT and Security Teams | Ensure compliance with government IT and security standards | High | Medium | Keep Informed: Regular consultations, involvement in technical reviews, and clear documentation of security protocols. |
| Citizens of NSW | End-users of the DXP, seeking access to government services | Low | High | Keep Informed & Engaged: Public announcements, user surveys, feedback portals, and co-design workshops. |
| Third-Party Vendors and Suppliers | Provide software, hardware, and services for the DXP | Medium | Medium | Monitor: Regular meetings, clear contractual agreements, and performance monitoring. |
| Media and Public Interest Groups | Influence public perception and hold the government accountable | Low | Medium | Monitor & Inform: Press releases, public demonstrations, and proactive communication on project milestones. |

## *6.2. Stakeholder Engagement Strategy:*

Building on the stakeholder analysis, the following engagement strategies will be employed to ensure effective communication and collaboration throughout the project lifecycle:

**Manage Closely (High Power, High Interest):** This group, which includes the Project Sponsor and key government agencies, requires the most intensive engagement. The strategy will involve:

• ***Regular One-on-One Meetings:*** Weekly meetings with the Project Sponsor to provide detailed progress updates, discuss key issues, and seek strategic guidance.

• ***Steering Committee:*** Establishment of a project steering committee with representation from key government agencies to provide oversight, make critical decisions, and ensure alignment with broader government objectives.

• ***Detailed Progress Reports***: Monthly progress reports detailing project status, key achievements, risks, and financial performance.

**Keep Satisfied (High Power, Low Interest):** This group, which includes IT and security teams, needs to be kept satisfied to ensure their support and cooperation. The engagement strategy will focus on:

• ***Regular Consultations:*** Proactive consultations to ensure that the DXP design and implementation align with government IT and security standards.

• ***Involvement in Technical Reviews:*** Inclusion of IT and security representatives in technical reviews and decision-making processes to address their concerns and leverage their expertise.

• ***Clear Documentation:*** Provision of clear and comprehensive documentation of the DXP architecture, security protocols, and compliance measures.

**Keep Informed (Low Power, High Interest):** This group, which includes the citizens of NSW, is critical to the project's success, as their adoption and satisfaction are primary objectives. The engagement strategy will be multifaceted and proactive:

• ***Co-design Workshops:*** A series of co-design workshops will be conducted with diverse groups of citizens to gather direct input on the DXP's design, functionality, and user experience. This will ensure that the platform is genuinely citizen-centric and meets the needs of its end-users.

• ***User Surveys and Feedback Portals:*** Regular user surveys and a dedicated feedback portal on the DXP will provide ongoing channels for citizens to share their experiences and suggestions for improvement.

• ***Public Announcements and Demonstrations:*** Regular public announcements and demonstrations of the DXP's progress and new features will keep citizens informed and engaged throughout the project lifecycle.

**Monitor (Low Power, Low Interest):** This group, which includes third-party vendors and the media, requires monitoring to ensure that their activities do not negatively impact the project. The engagement strategy will involve:

• ***Regular Meetings with Vendors:*** Regular meetings with third-party vendors to monitor their performance, address any issues, and ensure adherence to contractual agreements.

• ***Proactive Media Communication:*** Proactive communication with the media through press releases and public statements to manage public perception and ensure accurate reporting on the project's progress.

## *6.3. Agile-Inspired Communication Practices:*

To enhance stakeholder engagement and foster a culture of transparency and collaboration, the project will adopt several Agile-inspired communication practices:

### *Transparent Communication with Jira Dashboards:*

The project will utilize Jira dashboards to provide real-time visibility into project progress. These dashboards will be accessible to all relevant stakeholders and will display key metrics such as sprint burndown charts, task completion rates, and issue tracking. This will ensure that all stakeholders have a clear and up-to-date understanding of the project's status.

### *Regular Feedback Loops:*

Bi-weekly sprint reviews will provide a regular forum for the project team to demonstrate new features and gather feedback from stakeholders. This iterative feedback loop will ensure that the DXP is continuously aligned with stakeholder expectations and that any issues are identified and addressed early in the development process.

### *Daily Stand-ups:*

Daily stand-up meetings will be held with the project team to discuss progress, identify any impediments, and coordinate daily activities. This will foster a sense of shared ownership and ensure that the team remains focused and aligned on its goals.

### *Retrospectives:*

At the end of each sprint, a retrospective will be held to reflect on what went well, what could be improved, and what actions can be taken to enhance team performance in the next sprint. This commitment to continuous improvement will ensure that the project team is constantly learning and adapting its processes to optimize efficiency and effectiveness.

By implementing this comprehensive stakeholder management and engagement strategy, the DXP-SmartGovNSW project will foster a collaborative and transparent environment that is conducive to success. The integration of Agile principles will further enhance communication and collaboration, ensuring that the project remains responsive to the needs of its stakeholders and delivers a DXP that truly meets the needs of the citizens of NSW.

## 7. Project Monitoring and Change Control Strategy:

Effective communication and rigorous performance monitoring are indispensable for the successful execution of the DXP-SmartGovNSW project. This section details the strategies and mechanisms for ensuring timely, transparent, and relevant information flow among all

stakeholders, alongside the methods for tracking project progress and evaluating performance against established objectives and KPIs. The plan integrates both traditional project communication protocols and Agile-inspired practices to foster a collaborative and accountable environment.

## *7.1. Performance Monitoring:*

Project performance monitoring involves tracking, reviewing, and reporting progress to meet the performance objectives defined in Section 1. This continuous process allows the project team and stakeholders to understand the current state of the project, identify deviations from the plan, and take corrective actions promptly. The monitoring strategy focuses on key areas: scope, schedule, cost, and quality.

### *7.1.1. Tools and Techniques for Monitoring Performance:*

***Earned Value Management (EVM):*** For overall project performance, EVM will be utilized to integrate scope, schedule, and cost performance. Key EVM metrics such as Planned Value (PV), Earned Value (EV), and Actual Cost (AC) will be tracked. Variances (Cost Variance, Schedule Variance) and performance indices (Cost Performance Index, Schedule Performance Index) will provide quantitative insights into project health.

***Milestone Tracking:*** Progress against key milestones (as defined in Section 3) will be rigorously tracked. Achievement of milestones will be formally verified and communicated to stakeholders, serving as critical checkpoints for project progression. •

***Burndown Charts:*** For Agile development within sprints, burndown charts (Sprint Burndown and Release Burndown) will visually represent the remaining work versus time. This provides a clear, real-time indication of progress and helps identify potential delays early.

***Key Performance Indicators (KPIs) Dashboard:*** A centralized dashboard will be maintained to track the KPIs outlined in Section 1. This includes customer satisfaction scores, operational cost reduction, time-to-market for new services, system uptime, page load times, and user adoption rates. This dashboard will provide a holistic view of the project's impact and value delivery.

***Quality Metrics:*** Quality will be monitored through various metrics, including defect density, test coverage, and user acceptance testing (UAT) pass rates. Regular code reviews and automated testing will ensure adherence to quality standards.

***Risk Register Review:*** The risk register Section 5 will be reviewed regularly example weekly by the project team, monthly by the Steering Committee to monitor the status of identified risks, the effectiveness of mitigation strategies, and to identify any new risks.

### *7.1.2. Reporting Process:*

Performance data will be compiled into regular reports tailored to different audiences:

***Weekly Internal Status Reports:*** Concise reports for the project team and PMO, focusing on detailed task progress, immediate issues, and sprint performance metrics. These will often be derived directly from Jira dashboards.

***Monthly Executive Summary Reports:*** High-level reports for the Project Sponsor and Steering Committee, summarizing overall project health EVM, milestone achievement, budget summary, key risks, and strategic alignment. These reports will highlight progress against the project objectives and KPIs.

***Quarterly Business Reviews:*** Comprehensive reviews with senior management and key stakeholders to assess the project's strategic impact, return on investment, and alignment with broader organizational goals. These reviews will leverage the KPI dashboard and provide an opportunity for strategic adjustments.

## *7.2. Change Control Mechanism:*

Despite thorough planning and proactive risk management, changes are inevitable in complex projects. A formal change control mechanism is essential to manage these changes systematically, ensuring that they are evaluated, approved, and communicated effectively, minimizing their impact on the project objectives. The DXP-SmartGovNSW project will implement a structured change control process, integrated within the hybrid project management framework.

### *7.2.1. Change Request Process:*

Any proposed change to the project scope, schedule, or budget will follow a defined process:

***Change Request Submission:*** Any stakeholder internal team, client, vendor can submit a formal Change Request (CR) detailing the proposed change, its rationale, expected benefits, and potential impact on the project. CRs will be submitted via a designated project management tool example Jira.

***Initial Assessment:*** The Project Manager, in consultation with relevant team leads example Solution Architect, Business Analyst, will conduct an initial assessment of the CR to determine its feasibility, alignment with project objectives, and preliminary impact on scope, schedule, and budget.

***Impact Analysis:*** For approved CRs from the initial assessment, a detailed impact analysis will be performed. This involves quantifying the impact on:

• **Scope:** What new features or modifications are required? What existing features are affected?

• **Schedule:** How will the change affect activity durations, dependencies, and key milestones? Will it impact the critical path?

• **Budget:** What are the estimated costs associated with implementing the change example additional resources, software licenses, training?

• **Resources:** Are additional human or technical resources required?

• **Risks:** Does the change introduce new risks or alter existing ones?

***Change Control Board (CCB) Review:*** All significant CRs those with a medium to high impact on scope, schedule, or budget) will be reviewed by a Change Control Board (CCB). The CCB will comprise the Project Sponsor, Project Manager, key representatives from SmartGovNSW, and relevant technical leads. The CCB will evaluate the CR based on the impact analysis, strategic alignment, and available resources.

***Decision and Approval:*** The CCB will make a decision to:

• **Approve:** The change is approved and incorporated into the project plan.
• **Reject:** The change is not approved.
• **Defer:** The change is postponed for future consideration.
• **Request More Information:** Additional details are required before a decision can be made.

***Communication and Implementation:***

Once a CR is approved, the Project Manager will communicate the decision to all affected stakeholders. The project plan, WBS, schedule, and budget will be formally updated to reflect the approved change. The change will then be incorporated into the next appropriate sprint for implementation, following Agile principles for execution.

### *7.2.2. Agile Integration in Change Control:*

Within the iterative development sprints, minor changes and refinements are managed more fluidly. The Product Owner, in collaboration with the development team, can re-prioritize items within the product backlog for upcoming sprints without requiring a formal CCB review, as long as the changes do not significantly alter the overall project scope, budget, or timeline agreed upon by the CCB. This allows for rapid adaptation to evolving user needs and feedback. However, any changes that impact the agreed-upon sprint goals or introduce significant new work will be escalated to the Project Manager and potentially the CCB for formal review.

This integrated approach to risk management and change control ensures that the DXP SmartGovNSW project maintains its strategic direction while remaining agile and responsive to the dynamic environment of digital transformation.

# 8. Team and Individual Reflection:

## *8.1. Team Reflection:*

The development of this comprehensive Project Planning and Execution Strategy for the DXP-SmartGovNSW project was a collaborative effort that underscored the importance of effective teamwork and structured planning. Responsibilities were allocated based on individual strengths and expertise, ensuring that each team member contributed meaningfully to their respective sections.

Hari Krishna Jadda, with his background in full-stack development, focused on the technical aspects of the DXP, while Sankeerth Sappa, as a project management specialist, concentrated on the WBS and scheduling. Madhavi Latha Tripuram contributed her expertise in system integration and frontend-backend connectivity, and Dhimanshi Piripun Jayasena, as a lead quality engineer, ensured robust testing and quality assurance.

Prem Shanker Vanam provided valuable insights through technical analysis and research support. Collaboration was facilitated through regular virtual meetings, shared documentation platforms, and continuous communication channels, allowing for real-time feedback and iterative refinement of ideas.

A key lesson learned was the critical role of a well-defined WBS in breaking down complexity and providing a clear roadmap for execution. Furthermore, the iterative review process, mirroring Agile principles, proved invaluable in refining content and ensuring alignment with project objectives and stakeholder feedback. This collective effort reinforced the understanding that successful project planning is a dynamic and interconnected process, requiring constant communication and adaptability.

## *8.2. Individual Reflection:*

**Hari Krishna Jadda - Full Stack Developer & Systems Engineer:**

My contribution to this project primarily involved outlining the technical architecture, particularly the API-first and headless aspects of the DXP, and detailing the integration strategies. I also focused on the technical resource allocation within the budget estimates. This assignment deepened my understanding of how technical design decisions directly impact project timelines and resource needs. It highlighted the importance of clear, concise documentation for complex technical components to ensure seamless integration and deployment in a real-world context.

**Sankeerth Sappa - Project Management & Analytics Specialist:**

As the project management and analytics specialist, I was instrumental in developing the Work Breakdown Structure, project schedule, and defining the KPIs. I focused on ensuring that the project plan was structured, measurable, and aligned with the overall strategic goals. This experience reinforced the practical application of PMBOK principles and Agile methodologies in managing project complexity. It also improved my ability to anticipate challenges and align delivery methods with project objectives, which is crucial for successful project implementation.

**Madhavi Latha Tripuram - Software Engineer & Systems Integration:**

My role centered on defining the system integration aspects and contributing to the UI/UX considerations within the DXP. I focused on how various government systems would seamlessly connect with the new platform and ensuring a user-centric design. This task provided invaluable insights into the intricacies of large-scale system integration and the importance of a well defined integration strategy. It strengthened my understanding of how technical solutions must align with user needs and business processes for effective project delivery.

**Dhimanshi Piripun Jayasena - Lead Quality Engineer & Test Automation Specialist:**

My primary contribution was in shaping the quality assurance and testing strategies, including the integration of continuous testing within the Agile sprints and defining quality metrics. I focused on ensuring the reliability and robustness of the DXP. This assignment significantly enhanced my appreciation for proactive risk management and the role of comprehensive testing in mitigating project risks. It also underscored how a quality-first approach, integrated throughout the project lifecycle, is essential for delivering a high-quality product in a real-world setting.

**Prem Shanker Vanam - IT Specialist & Technical Analyst:**

My contribution involved conducting technical analysis, supporting research for emerging technologies, and assisting with documentation. I focused on ensuring that the proposed solutions were technically sound and well-supported by current industry practices. This experience broadened my understanding of the foundational research and analytical work required for robust project planning. It also provided practical exposure to how theoretical knowledge translates into actionable strategies in a complex project environment, enhancing my analytical thinking and problem-solving skills.

## 9. References:


- Digital NSW. (n.d.). Experience Management. Digital.NSW. https://www.digital.nsw.gov.au/explore-design/experience-management

- NSW Government. (2023). Digital Strategy for the NSW Government. https://www.digital.nsw.gov.au/strategy-policy/nsw-digital-strategy

- Digital NSW. (n.d.). Plan a Project. Digital.NSW. https://www.digital.nsw.gov.au/deliver-and-innovate/project-delivery

- Digital Transformation Agency (Australia). (2023). Digital Experience Policy. https://www.dta.gov.au/help-and-advice/policies-and-guides/digital-experience-policy

- Australian Government. (2023). Digital Experience Policy and Standards Announcement. https://www.digital.gov.au/news/announcing-australias-digital-experience-policy-and-standards

- NSW Government. (2024). Digital Experience Platform – Request for Proposal. https://buy.nsw.gov.au/tenders/dxp-rfp

- Digital NSW. (2024). Digital NSW 2024 Showcase. https://www.digital.nsw.gov.au/showcase-2024

NSW Government. (2025). Digital Transformation Strategy 2025. Retrieved from https://www.nsw.gov.au/digital-transformation-strategy-2025

Project Management Institute. (2017). A Guide to the Project Management Body of Knowledge (PMBOK® Guide) (6th ed.). Project Management Institute.
